Project Manager: James Monday

KING HALL RENOVATION & EXPANSION

Project No. 9503400

Updated: 5/1/08

ID	Phase	Weeks	Progress to date	Start	Finish
1	**Preliminary Plans**	31 wks	100%	Sat 7/1/06	Fri 2/2/07
2	**SPWB Approval**	10 wks	100%	Mon 2/5/07	Fri 4/13/07
3	**Design Approval**	0 wks	100%	Mon 12/11/06	Mon 12/11/06
4	**Working Drawings 1**	96 days	100%	Fri 7/6/07	Thu 11/22/07
5	**Agency Review 1**	4.9 wks	100%	Fri 10/26/07	Thu 11/29/07
6	**Bid & Award Addition**	13 wks	50%	Fri 2/1/08	Thu 5/1/08
7	**Construction Addition**	347 days	0%	Fri 5/2/08	Mon 8/31/09
8	**Working Drawings 2**	22 wks	0%	Fri 5/2/08	Thu 10/2/08
9	**Construction Renovation**	261 days	0%	Wed 7/1/09	Wed 6/30/10
10	**Occupancy Addition**	0 days	0%	Mon 8/31/09	Mon 8/31/09
11	**Occupancy Renovation**	0 wks	0%	Wed 6/30/10	Wed 6/30/10
12	**Close Out**	12 wks	0%	Thu 7/1/10	Wed 9/22/10

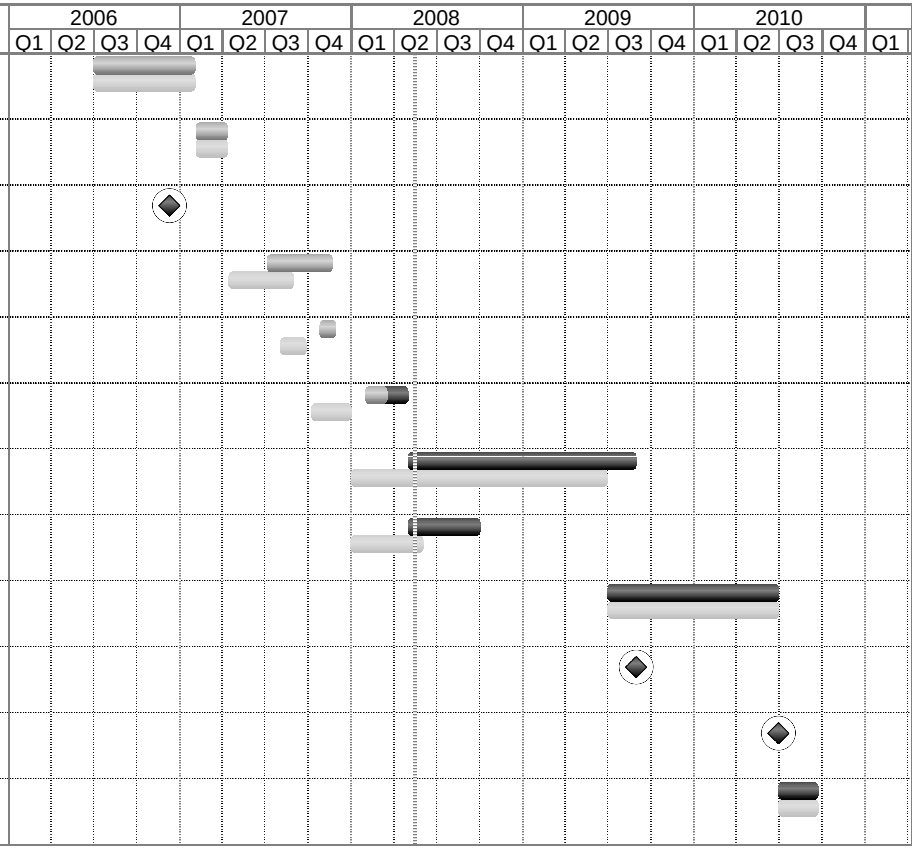

PPG Schedule

Current Schedule

PPG Occupancy Date

Milestone

Progress to date
